

April 2017 CONSTRUCTION UPDATE


WORK PROGRESS

Roof installation began over the YMCA along Southdale Road beginning the process of making the building water tight. Work continued on the lap and leisure pools preparing them for the surrounding concrete deck as well as the bottom of the leisure pool.

The arenas are taking form as the steel deck is being installed on Rink 1 and the remaining structural steel over Rink 2. Structural steel and core slab was installed back of house of the arenas in preparation of the mechanical equipment to be installed in the boiler room.

As steel roof deck installation continues over the Gathering Area, the openness of this space and the views to all programs within the building is becoming evident, an objective desired by the City of London from the beginning of the design process.

PHOTOS

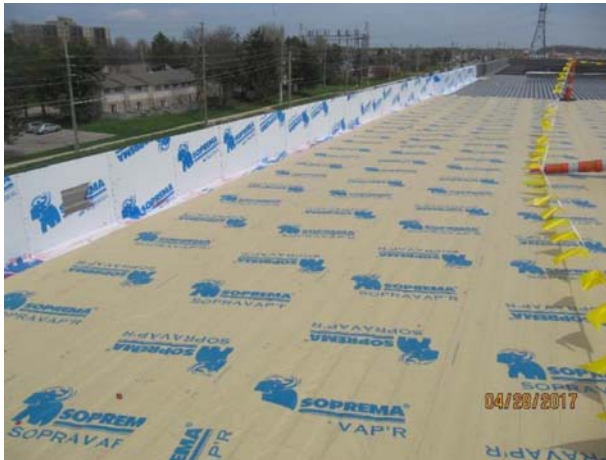

1. Roof view looking East along Southdale.



2. Roof view with skylight in the background.



3. Lap pool – preparation of base for deck install



4. Leisure pool – preparation for concrete placement



5. Rink 1 – enclosing with steel decking



6. View from fitness across gathering area to Service London and walking loop.



7. Rink 2 and back of house loading area

PREPARED BY THE CONSULTANT:

MJMA / a+LiNK

Ed van der Maarel

ARCHITECT, OAA, CAHP

a+LiNK architecture Inc. Partner
