

## August 2017 CONSTRUCTION UPDATE

### WORK PROGRESS


During the month of August work continued on the interior of the building with the primary focus on preparing the two rinks for placement of the concrete slab. This precise process continues towards two pours, Rink 1 late September and Rink 2 in early October.

The gathering space stairs and seating area also continued to take shape as each section had to be independent placed due to the substructure slope. The interior work within the gathering space continues as well and now provides a sense of space with full view of the whole facility.

Roof construction continues to progress while curtainwall and glazing was a major focus on the exterior of the building to close it in for rink concrete pours. Aluminum curtainwall was installed on the west elevation and front elevation in preparation for the site measurement for the precast base around the building.

Masonry installation is underway with the white brick upper façade juxtaposed with the grey brick base providing a sense of founding of the building. Masonry will continue along the south side of the building at Rink 2 and continue to the Library during September.

### PHOTOS

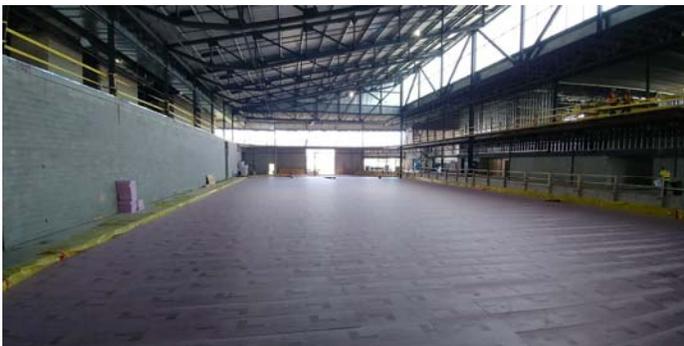

1. View of the preparation of Rink 1.



2. View of the preparation of Rink 2.



3. Interior view of Fitness towards upper Aquatics area.



4. Walking loop above Rink 1.



5. Glazing installation on clerestory skylight for Rink 1.



6. Site view looking north towards south entrance.



7. Cladding substrate east plaza.



8. Curtainwall installation gymnasium

PREPARED BY THE CONSULTANT:

**MJMA / a+LiNK**

Ed van der Maarel

ARCHITECT, OAA, CAHP, a+LiNK architecture Inc. Partner
