

February 2018 CONSTRUCTION UPDATE

WORK PROGRESS

February was another month with a lot of snow and therefore the sub trades continued diligently on the interior of the building. The project remains on schedule with only four months from the handover date from the Design and Construction Team to the Owner.

Railings and hanging systems are starting to come together in the Gathering Space for completion of the ceiling systems while surrounding interiors of the Library, Rinks, and YMCA come together. Transparency through to all spaces is a key design feature of the facility and glass was being installed everywhere throughout the facility in the month of February.

Some of finishes are in the advance preliminary stages with Change Rooms being tiled and paint being applied in those areas that can be fully completed. The rinks will be handed over shortly to the trades installing the rink boards and glass in anticipation for final completion.

PHOTOS



1. View of exterior looking northwest



2. Gathering space framing under way



3. Gathering space railing for the Walking Loop to the right



4. Rink 1 finishes under way



5. Rink 1 finishes under way



6. Rink 1 viewing area in progress



7. Rink 2 finishes under way



8. Aquatics Hall in progress




9. Open Fitness view to Aquatics Hall



10. Library glass installation in progress



11. Library mezzanine glass installation in progress

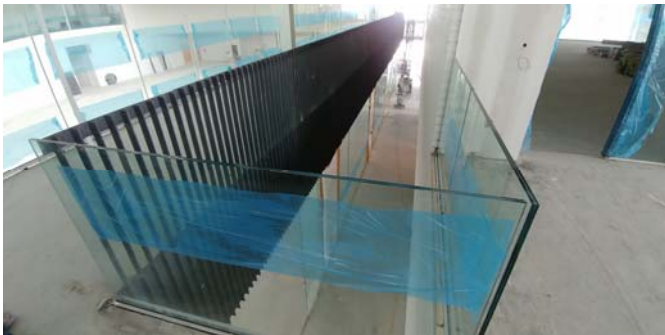

12. Walking Loop glass installation in progress



13. Walking Loop view into Rink 1

PREPARED BY THE CONSULTANT:
MJMA / a+LiNK
Ed van der Maarel,
ARCHITECT, OAA, CAHP, a+LiNK architecture Inc. Partner
