

October 2017 CONSTRUCTION UPDATE

WORK PROGRESS

Work on the project continues at an amazing pace. The interior spaces for the Library are taking shape on both Levels with ongoing metal stud work in preparation for drywall installation. The Aquatics Hall also continues to take shape with ongoing water tests for both the lap pool and the leisure pool. The north seating bench has been formed and concrete is curing prior to installation of the tile. The piping and concrete floors for Rink 2 was also placed in October in preparation for finishing the interiors of the both rinks.


Exterior masonry is near completion and curtainwall is ongoing to close the building in for the winter and continuation of the interior finishes. Masons will move to the interior spaces as the weather becomes colder.

A base coat of asphalt was placed in the south parking lot, which concludes work in this area until Spring thaw. Work crews concentrate on the interior spaces over the winter months in order to meet the Summer 2018 completion date.

PHOTOS



1. View of Library Mezzanine Stair

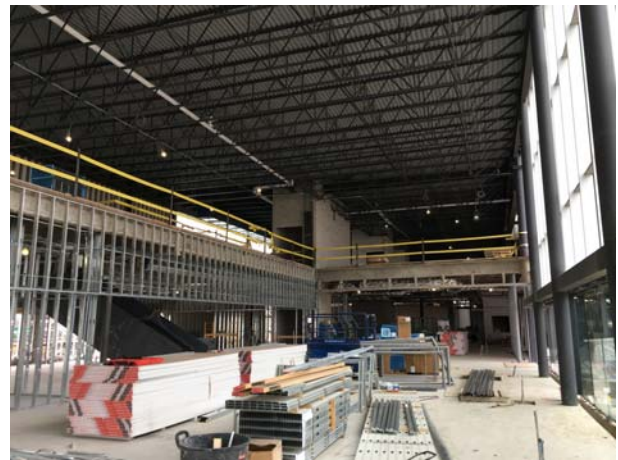

2. Library interior metal stud in progress.



3. Aquatics Hall north bench seating.



4. Leisure Pool water test in progress.



5. Rink 2 concrete slab and piping placed.



6. View of North façade.



7. View to East Plaza.



8. View from parking lot to South building entrance.

PREPARED BY THE CONSULTANT:
MJMA / a+LiNK
Ed van der Maarel, ARCHITECT, OAA, CAHP, a+LiNK architecture Inc. Partner
