

September 2017 CONSTRUCTION UPDATE

WORK PROGRESS

The concrete floor for Rink 1 was placed in September meeting the strict criteria for flatness over the length and width of the rink slab. Rink 2 piping and insulation installation took place in preparation for placement of the concrete slab in October.

Work continued in all areas of the interior spaces with the installation of the electrical and mechanical systems which eventually will be hidden behind the features of the ceilings and walls. A mockup of the guards and railings was reviewed by the project team in anticipation of full installation around the Walking Loop above Rink 1.

On the exterior, the work on the curbs and sidewalks began on the South side of the site in preparation for base coat asphalt to be applied in October. Curtainwall and masonry continued on the exterior of the facility in order to meet a milestone of closing the building in for winter by the end of November.

PHOTOS



1. View Rink 1 concrete placement in progress.




2. View Rink 1 concrete placement in progress.



3. Gathering Area in progress.



4. Mockup of picket construction for Walking Loop.

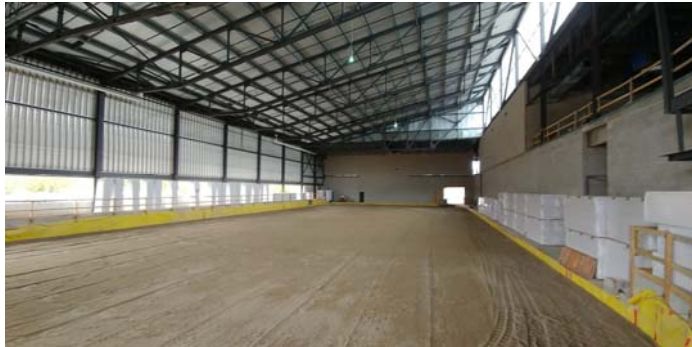

5. View of the preparation of Rink 2.



6. South parking lot curbs in progress.



7. North façade masonry and curtainwall.



8. Curtainwall installation Library north façade.



9. View of South of facility looking north to south entrance.

PREPARED BY THE CONSULTANT:

MJMA / a+LiNK

Ed van der Maarel, ARCHITECT, OAA, CAHP, a+LiNK architecture Inc. Partner
